

San Bernardino County Transportation Authority
MAJOR PROJECTS
PROJECT STATUS REPORT
July – September 2025



1170 West Third Street, Second Floor
San Bernardino, California 92410-1715
Telephone: (909) 884-8276
www.gosbcta.com

ORDER OF PROJECT DELIVERY



TABLE OF CONTENTS

Page No.

Project Location Maps

1 Mainline Projects

2 Interchange Projects

3 Grade Separation Projects

4 Special Projects

	<u>Project Name</u>	<u>Phase</u>	<u>Corridor</u>
	Mainline Projects		
5	I-10 Corridor (Contract 1)	Design-Build/ROW	I-10
6	I-10 Corridor (Contract 2)	Design/ROW	I-10
7	I-10 EB Truck Climbing Lane	Close Out	I-10
8	SR-210 Lane Addition	Landscape	SR-210
9	I-15 Corridor (Contract 1)	Construction	I-15
10	I-215 Bi-County/Segment 5 Landscape	Design	I-215
11	I-215 Widening Seg 2 Landscape	Close Out	I-215
12	US-395 Widening Project - Phase 2	Design/ROW	US-395
13	SR-62 Sage to Airway Avenue	Planning	SR-62
14	SR-18 Median Widening and Reprofiting	Environmental	SR-18
15	I-15 Cajon Pass NB TCL extension	Planning/Environmental	I-15
	Interchange Projects		
16	SR-60 / Central Avenue	Landscape	SR-60
17	I-10 / Cedar Avenue	Construction	I-10
18	I-10 / Mount Vernon Avenue	Design/ROW	I-10

(Continued)

Page No.

	<u>Project Name</u>	<u>Phase</u>	<u>Corridor</u>
19	I-10 / Alabama Street	Close Out/Landscape	I-10
20	SR-210 / Base Line	Landscape	SR-210
21	I-15 / I-215 Improvement (Devore)	Close Out	I-15 & I-215
22	I-215 / Barton Road	Close Out	I-215
23	I-215 / University Parkway	Construction	I-215
24	SR-210 Waterman Avenue	Construction	SR-210

Grade Separation Projects

25	Monte Vista and UPRR	Close Out	Local Streets
26	Mount Vernon Avenue Viaduct	Design-Build/ROW	Local Streets
27	North First Avenue Bridge over BNSF	Close Out	Local Streets

Special Projects

28	Metrolink ATP (Phase II)	Construction	Local Streets
29	Highland/Redlands Reg Gap Connector	Environmental/Design	Local Streets

Note:

1. "Board Approved Funding" amounts at the start of each project reflect the latest approved 10-Year Delivery Plan amounts. The 10-Year Delivery Plan amounts by phase are superseded as cooperative agreements are approved and executed.
2. "Construction" under each project's "Budgetary Estimate at Completion (\$000's)", in addition to construction capital costs, includes costs associated with construction management, landscaping and any other estimated construction expense.

PROJECT STATUS -DEFINITIONS-

Complete for Beneficial Use: Satisfactory completion of the project's stated purpose to allow public use of facilities without restrictions.

Construction: Project phase after Construction Notice to Proceed (NTP) through end of Project.

Closeout: Construction complete and completing formal close out of all contracts.

Board Approved Funding: Funding approved by the SBCTA Board, which supersedes the funding approved in the 10-Year Delivery Plan.

Design & ROW: Project phase after Project Report (PR) Approval and before Construction NTP.

"Early": Work along a Mainline or Segment that is performed first to assist execution of a major project.

EEP: Establish Existing Planting

End of Project: Final completion of all construction activities and formal Close Out of construction contracts and ROW activities.

Environmental Clearance: Project phase after Project Initiation Document (PID) approval. Includes development of Project Approval (PA) documentation, and Environmental Documents (ED).

Final Design Approved: Completion of all design activities and environmental certifications and ROW.

Grade Separation: Work to change elevations of road and/or rail intersections to expedite traffic flow.

HOV: High Occupancy Vehicle (i.e. car pool).

Interchange: Connectors between Interstates and/or major roads.

Interstate Highway: Federally monitored high speed roads.

Local Streets: State/City owned and maintained streets.

Mainline: Interstate freeway corridor project that is new and/or widened (added lanes - general purpose, HOV, auxiliary, etc.).

NTP: Notice to Proceed.

Planning: Project phase after Start of Project and before Project Study Report (PSR) Approval.

Preliminary Engineering: Part of the Environmental Clearance phase that includes the design effort required to sufficiently define the project's alternatives and support the development of the Environmental Documentation (ED). Completion of preliminary engineering will approximate 30% of the overall design effort of the project.

Project Initiation Document (PID): Report documenting the early scoping definition of a project used to determine viability of proceeding with Preliminary Engineering and Environmental approvals, project alternatives and preliminary project costs by phase.

Project Report (PR): Report documenting the Preliminary Engineering (up to 30% of Design) to recommend the preferred alternative used for Project Approval (PA). All Environmental Documentation (ED) is contained in this report.

PS&E: Development of the final Plans, Specifications and Estimates for use in bidding the construction.

Right-of-Way (ROW): Identification, appraisal and purchase of required land parcels for the project. Also includes the right of possession of land through condemnation. ROW Certification is a prerequisite for Construction bidding.

RTL: Ready to List.

Segment: A specified portion of an Interstate freeway corridor project that is widened (added lanes - general purpose, HOV, auxiliary, etc.).

Sound Walls: Self supported walls that are of sufficient height to reduce roadway noise to an acceptable level.

Start of Project: Board action to begin project.

Utility Relocation: Modification of all utilities (i.e. Electrical, Gas, Water, Sewer, Communications, etc.) to alleviate conflicts with project's construction or use. Utility Certification is a prerequisite for Construction bidding.

PROJECT STATUS

-FUNDING PROGRAM DESCRIPTIONS-

FEDERAL

- ARRA – American Recovery and Reinvestment Act
- ATP – Active Transportation Program
- CMAQ – Congestion Mitigation & Air Quality Program
- DEMO – Demonstration Project
- EARREPU – Earmark Repurposing Fund
- HBP – Highway Bridge Program
- IMD – Interstate Maintenance Discretionary
- PNRS – Project of National & Regional Significance
- STP – Surface Transportation Program
- TE – Transportation Enhancement
- TEA – Transportation Enhancement Activity
- TIFIA – Transportation Infrastructure Finance and Innovation Act
- TIGER – Transportation Investment Generating Economic Recovery


STATE

- CMIA – Corridor Mobility Improvement Account
- ITIP – Interregional Transportation Improvement Program
- IIP – Interregional Improvement Program
- LPP – Local Partnership Program (Senate Bill 1)
- PUC – Public Utilities Commission
- RIP – Regional Improvement Program
- SHOPP – State Highway Operation and Protection Program
- SLPP – State Local Partnership Program
- STIP – State Transportation Improvement Program
- TCEP – Trade Corridor Enhancement Program (Senate Bill 1)
- TCIF – Trade Corridor Improvement Fund
- TCRP – Traffic Congestion Relief Program
- TIRCP – Transit and Intercity Rail Capital Program
- TLSP – Traffic Light Synchronization Program


LOCAL

- DIF – Developer Impact Fees
- IVDA – Inland Valley Development Agency
- TDA – Transportation Development Act
- WVWD – West Valley Water District

PROJECT LOCATION MAP MAINLINE PROJECTS

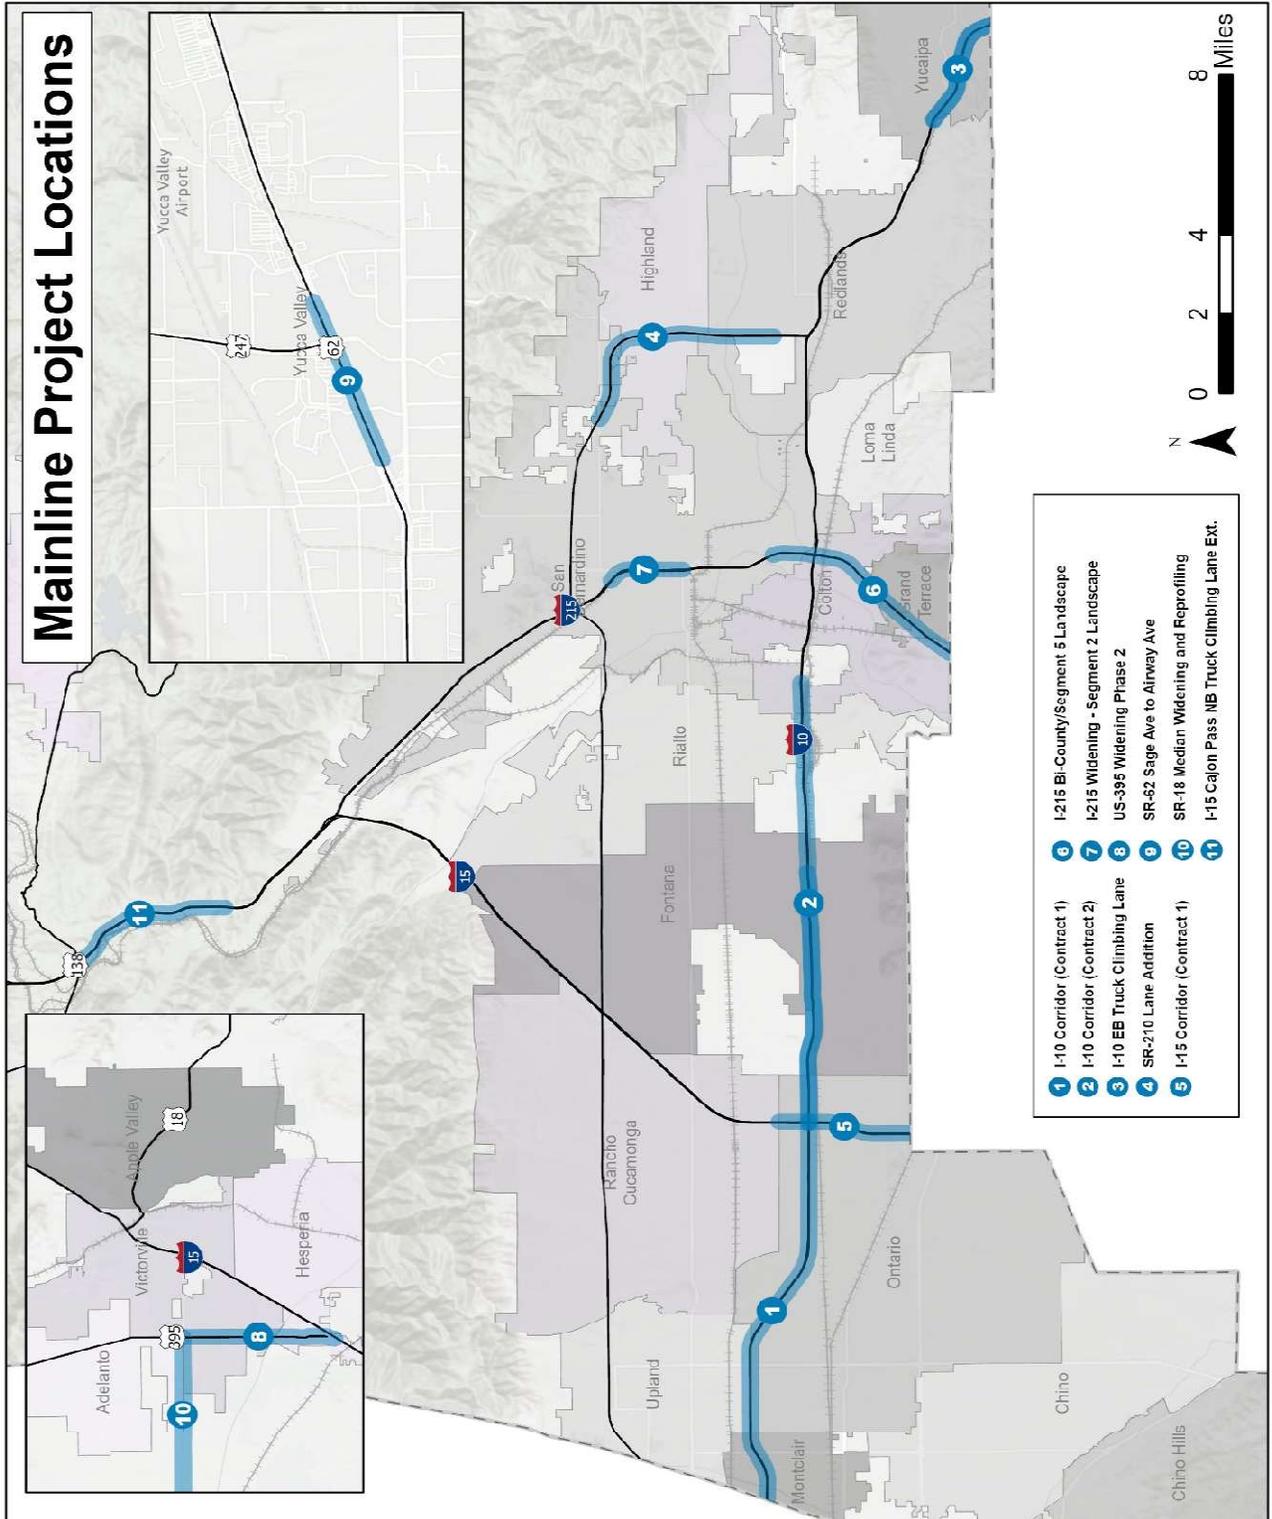


PROJECT LOCATION MAP INTERCHANGE PROJECTS

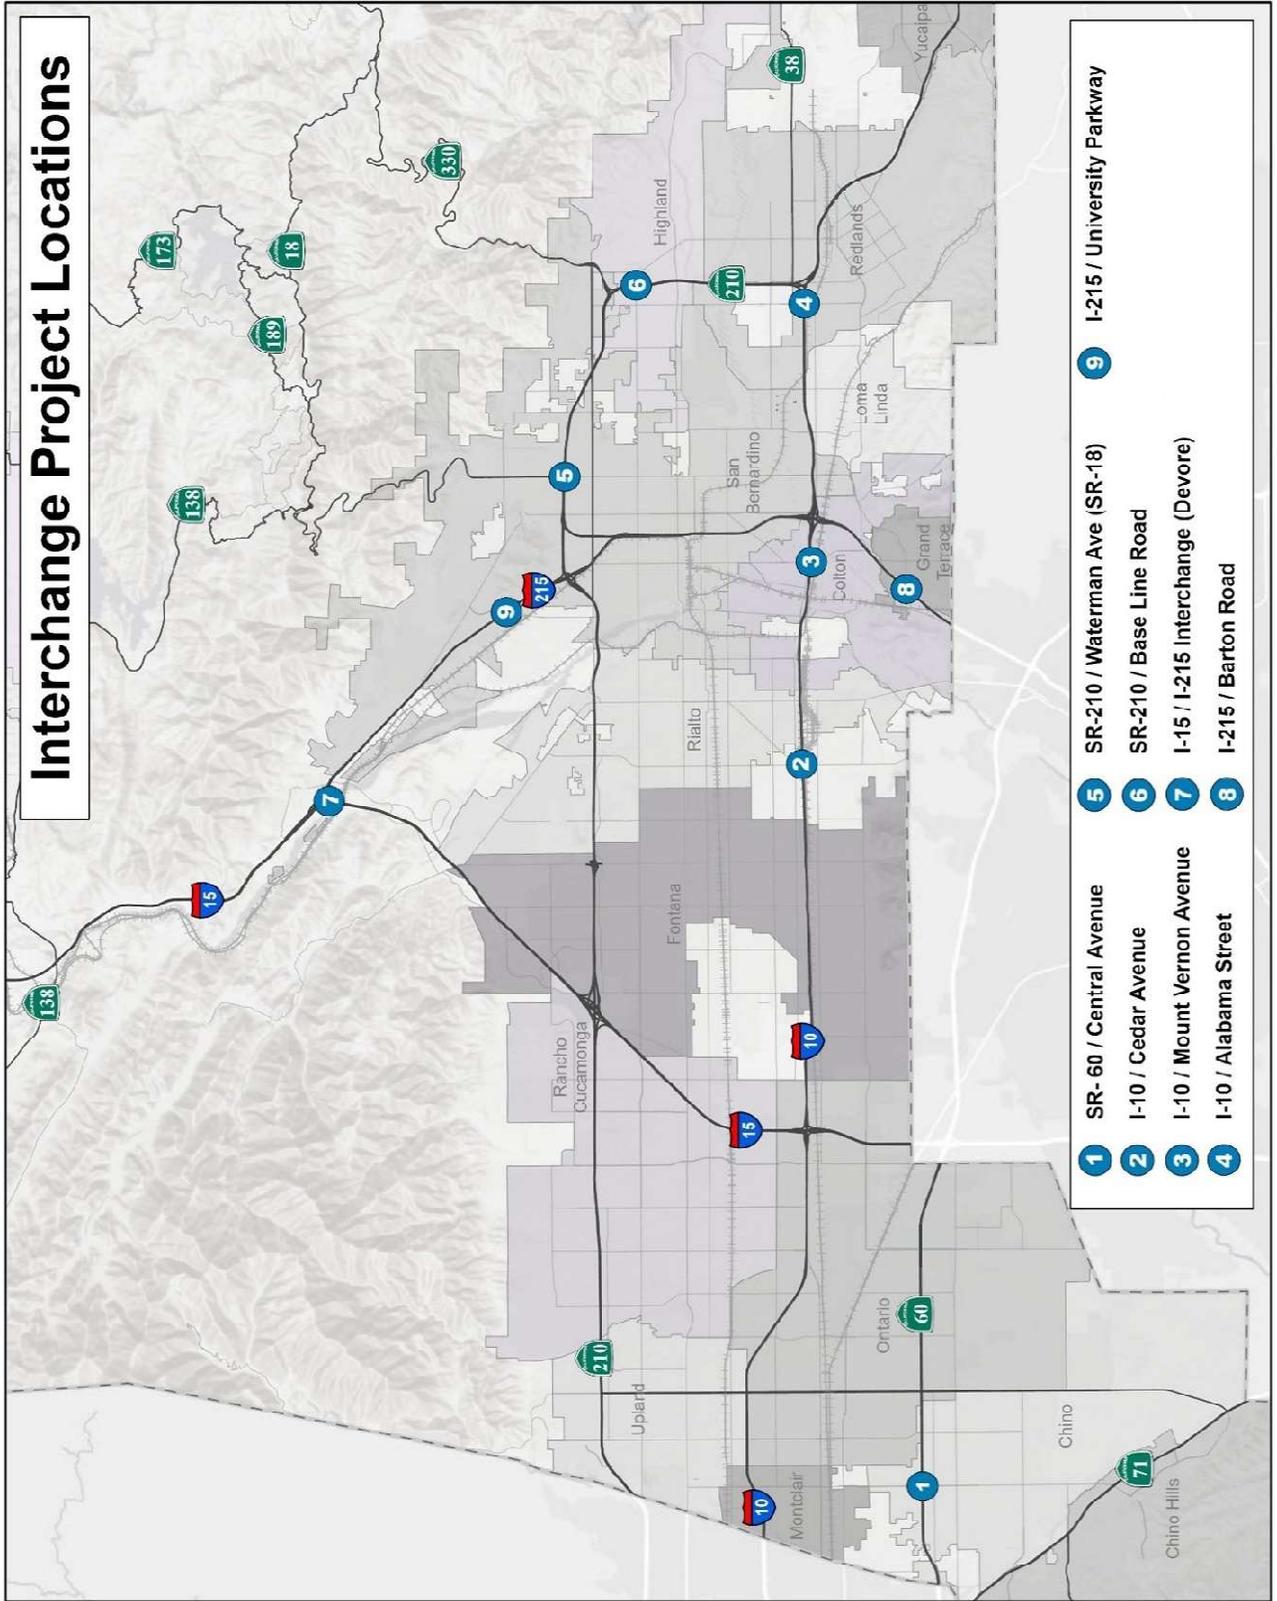


SAN BERNARDINO COUNTY TRANSPORTATION AUTHORITY
 PROJECT DELIVERY – KRISTI HARRIS, DIRECTOR
 PROJECT STATUS – SEPTEMBER 2025

**PROJECT LOCATION MAP
SPECIAL PROJECTS**

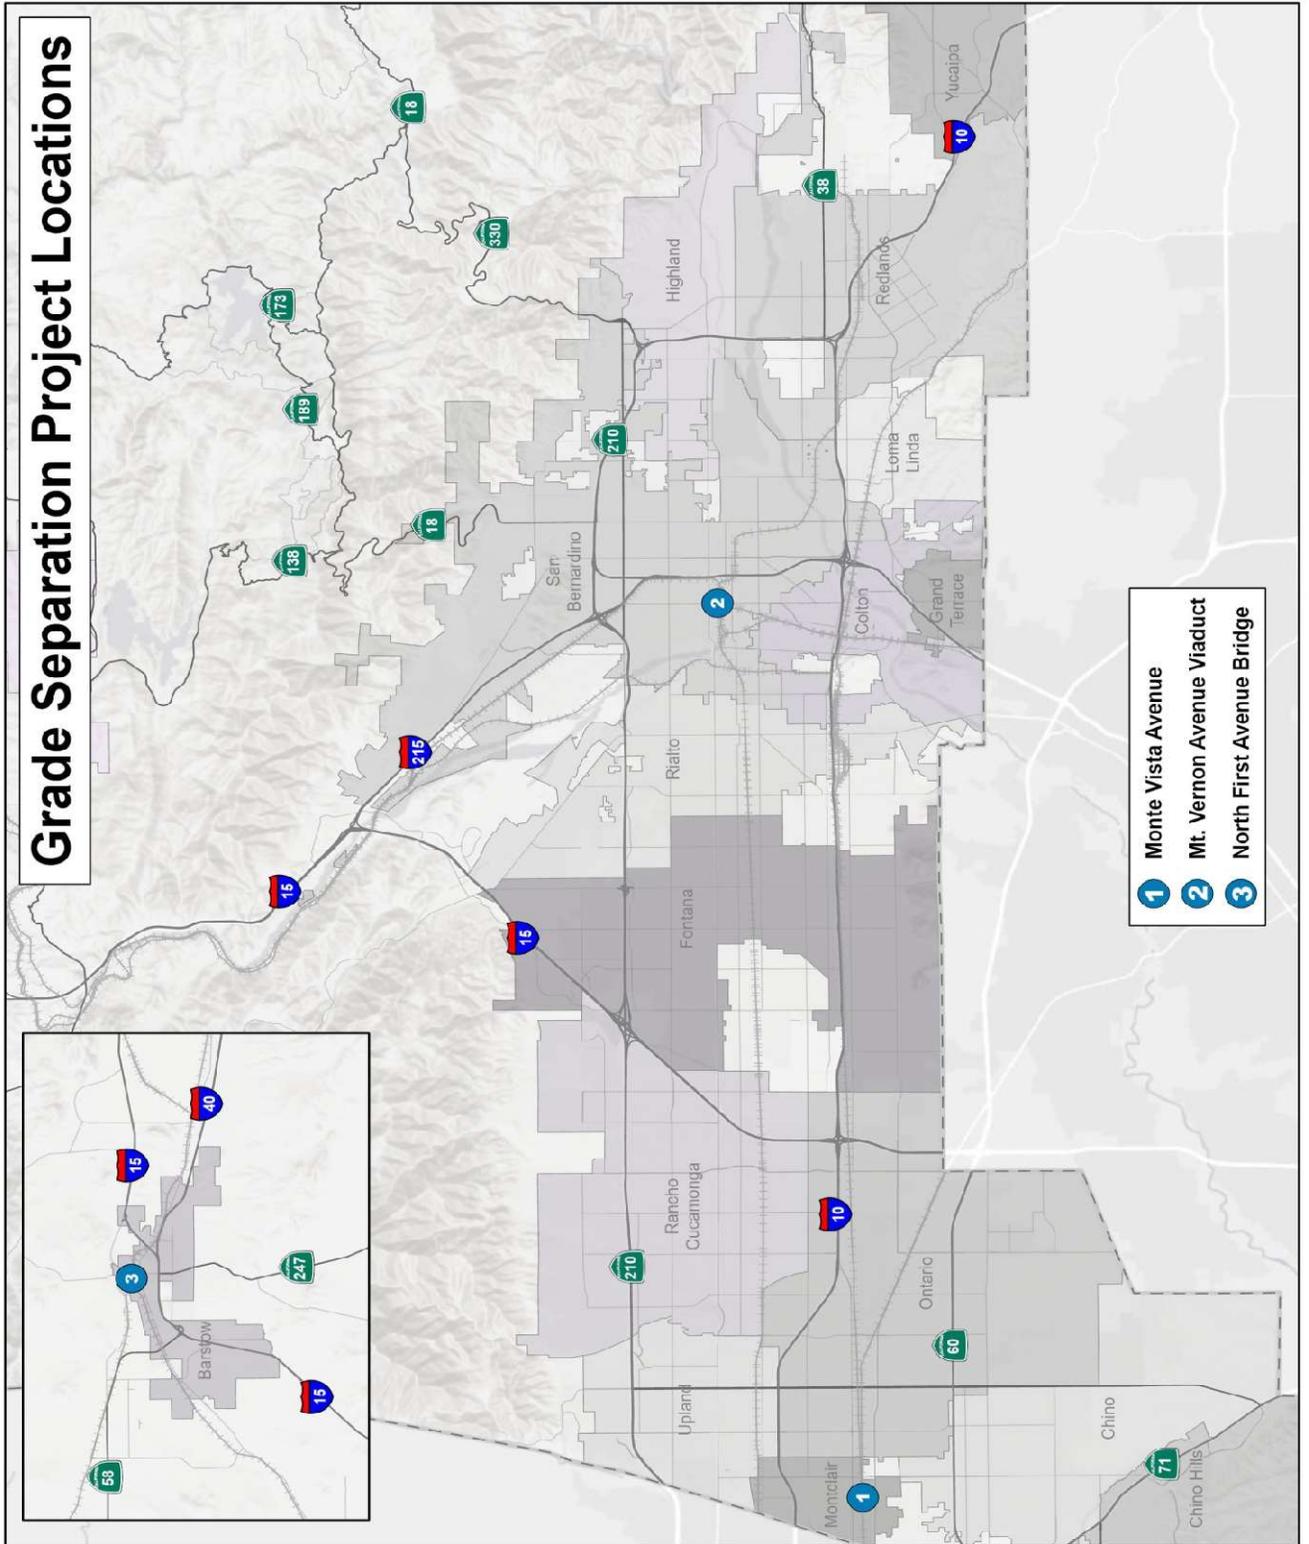


**PROJECT LOCATION MAP
SPECIAL PROJECTS**

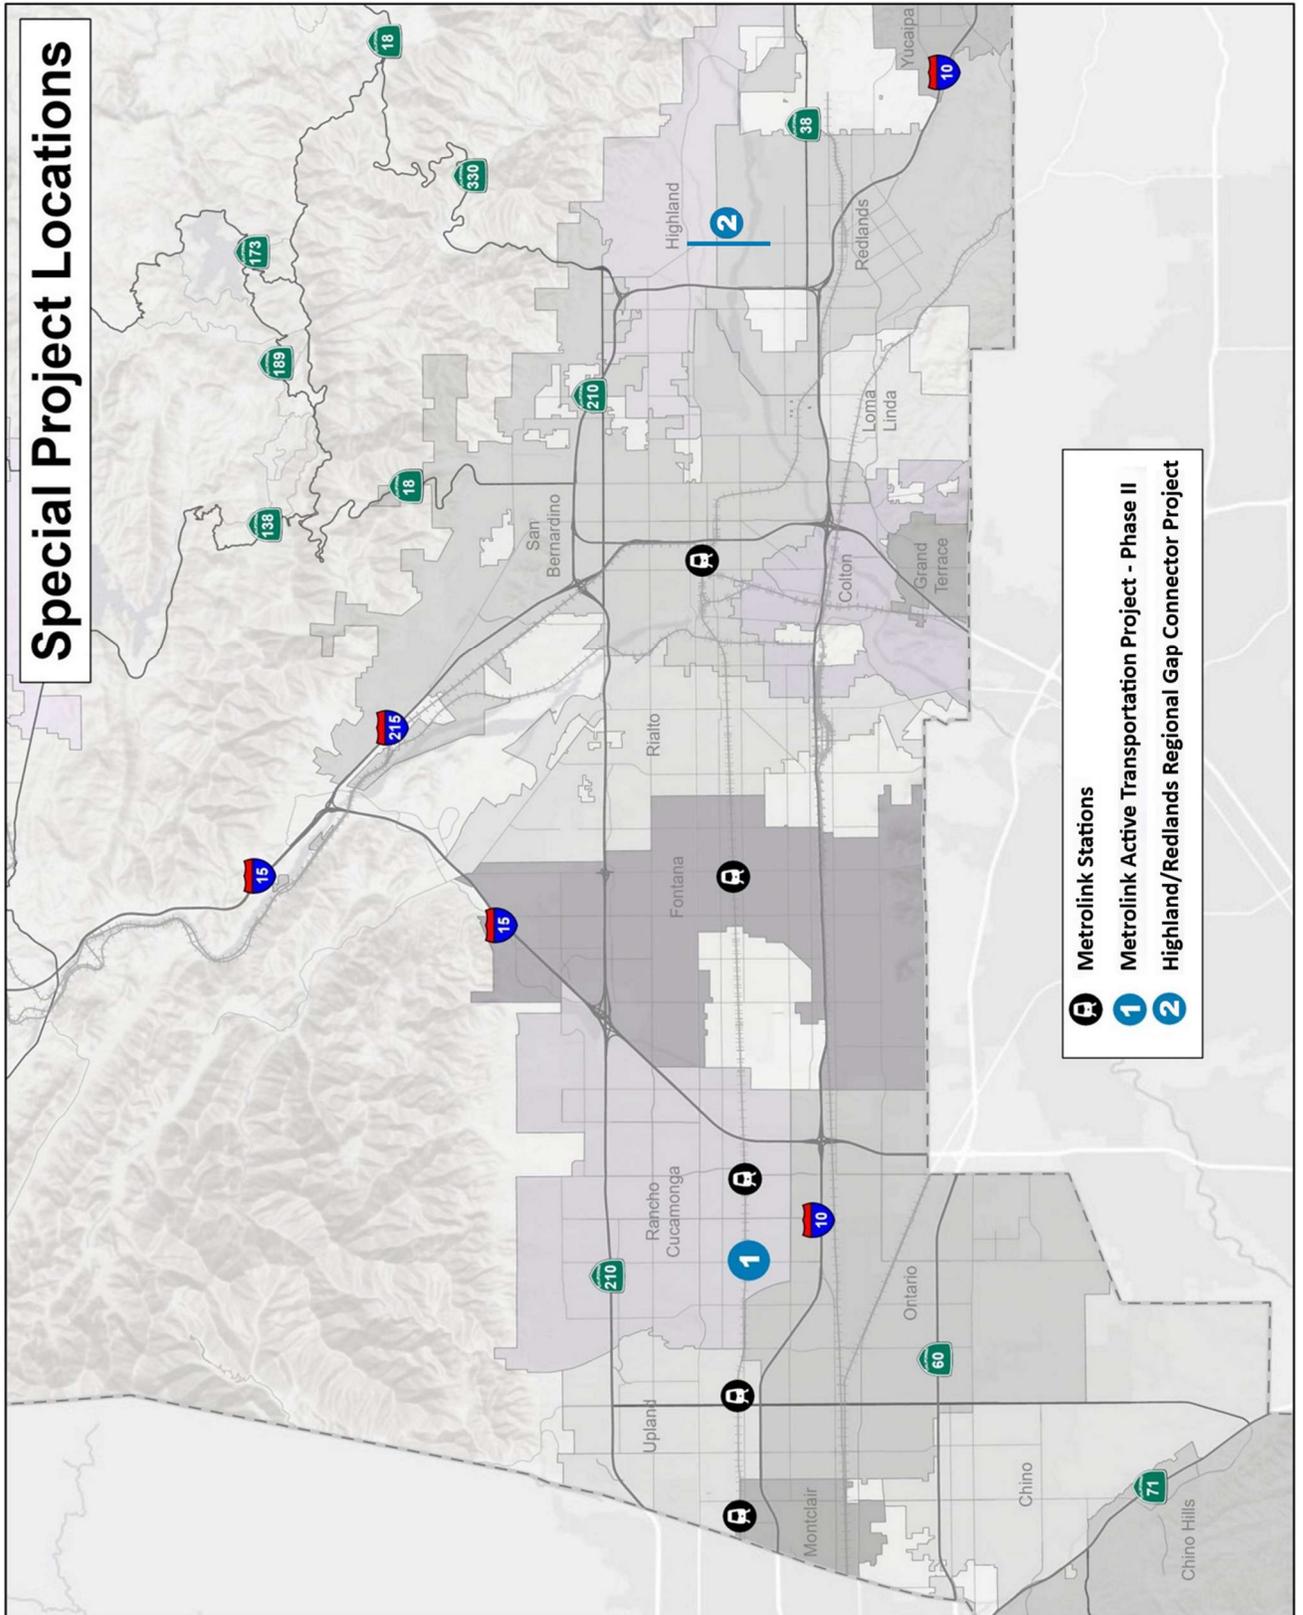

SAN BERNARDINO COUNTY TRANSPORTATION AUTHORITY
 PROJECT DELIVERY – KRISTI HARRIS, DIRECTOR
 PROJECT STATUS – SEPTEMBER 2025

I-10 CORRIDOR FREIGHT AND EXPRESS LANE PROJECT (Contract 1)

Map of Project:

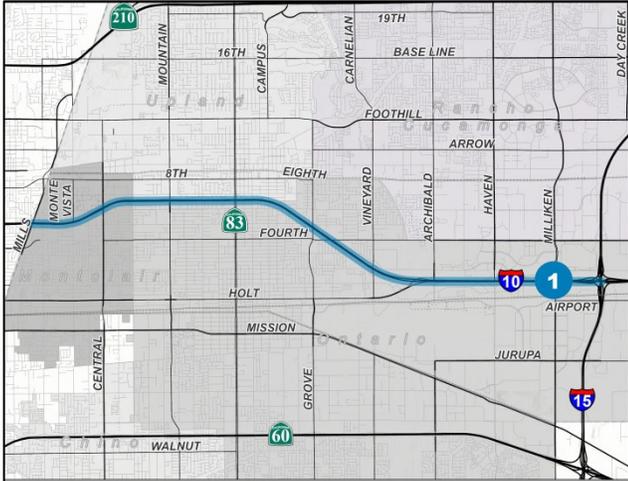

Project Scope Summary:

This project provides express lanes along the I-10 in each direction from the Los Angeles County line to I-15, approximately 10 miles.

Project Status and Continuing Activities:

- Design Builder final design and field investigation work for utilities and geotechnical work are complete.
- Toll System Provider (TSP) NTP 2 work began in February 2019. Toll system final design was completed in July 2022 and Factory Acceptance Testing (FAT) was completed in September 2022 and TSP field work finished, with Revenue Commencement initiated in late August 2024.
- ROW acquisition is completed in Montclair, Upland, and Ontario and staff is continuing to manage active Temporary Construction Easements and close out final agreements as necessary.
- Utility relocation work is approximately 99% complete, though minor punch list work continues at various locations along I-10, performed by LSPJV.
- I-10 Mainline widening construction work is nearly finished between Los Angeles County line to Etiwanda Avenue (12 miles), including final bridge construction at 6th Street, Euclid, Monte Vista, San Antonio, Sultana, Vineyard, Holt, and Campus Avenue bridges, with operational express lanes open since August 2024.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Jul 2007
Project Initiation Document (PID) Approved (by others)	Jun 2005
Environmental Clearance (PA/ED)	Jul 2017
Construction NTP 1 Design Build	Sep 2018
Construction NTP 2	Mar 2019
Complete for Beneficial Use	[Nov 2025]
End of Project	[Jan 2027]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Study Report	-Caltrans-
Project Report EIR	\$8,828
Final Design	\$44,246
ROW	\$53,300
Construction	\$856,669
Total	\$963,043

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Federal – CMAQ/STP	\$289,059
Federal – TIFIA	\$225,000
State SHOPP	\$117,755
Measure I/City	\$162,511
State STIP/RIP	\$39,745
State TCIF	\$4,973
State LPP	\$6,169
TCEP	\$117,831
Total	\$963,043

Board Approved Funding: \$963,043,000

Project Notes of Interest:

- Staff continues close coordination with the Cities of Ontario, Montclair and Upland to draft the Freeway Maintenance Agreements and coordinate project reviews and inspections required for the close-out of construction permits.
- Final project costs approved in June 2018 also includes cost of Caltrans SHOPP work and local interchange and arterial improvements, constructed as part of the Project.

Lead Agency: SBCTA

Project Manager: Chad Costello (909) 884-8276
ccostello@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

I-10 CORRIDOR FREIGHT AND EXPRESS LANE PROJECT (Contract 2)

Map of Project:



Project Scope Summary:

This project provides a single express lane, in each direction, along the I-10 from the Interstate 15, in the City of Ontario, to Pepper Avenue, in the City of Colton, a length of approximately 11 miles, connecting to the I-10 Corridor Contract 1 express lanes currently in operation.

Project Status and Continuing Activities:

- The Project will be delivered as a traditional methodology (Design-Bid-Build), including the Toll Collection System Design Elements. The design consultant has been selected and was awarded a design contract at the July 6, 2022 Board meeting.
- To expedite Project delivery, the Project will be divided into two construction contracts: Contract 2A from Interstate 15 to Sierra Avenue and Contract 2B from Sierra Avenue to Pepper Avenue.
- The 100% Design, Supplemental Project Report, Environmental Revalidation, and Right-of-Way Certification for Contract 2A have been approved by Caltrans.
- The 95% Design and Right-of-Way tasks for Contract 2B are in progress.
- Contract 2A achieved its Ready-to-List milestone in June 2025 and an Invitation for Bids was released on September 18, 2025.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Jul 2007
Project Initiation Document (PID) Approved (by others)	Jun 2005
Environmental Clearance (PA/ED)	Jul 2017
Final Design Approved (RTL), Segment 2A / 2B	Jun 2025 / [Jan 2026]
Construction NTP Segment 2A / 2B	[Jan 2026 / Jul 2026]
Complete for Beneficial Use	[Dec 2028]
End of Project	[Mar 2030]

Project Notes of Interest:

- Project will improve eastbound acceleration lanes between Cherry Ave and Citrus Ave and Sierra Ave to Cedar Ave; and add auxiliary lanes in both directions from Riverside Ave to Pepper Ave.
- Project includes interchange ramp modifications at Etiwanda Avenue; Cherry Avenue; Citrus Avenue; Sierra Avenue; Cedar Avenue; Riverside Avenue; and Pepper Avenue.
- Project will include structure widening, replacement, or abandonment at Day Creek Channel (widen); Etiwanda Wash (widen); Valley Blvd Exit Ramp Undercrossing (widen); Etiwanda-San Sevaine Channel (widen); Etiwanda-San Sevaine Channel Ramp (replacement); Kaiser Spur Overhead (widen); San Sevaine Creek (abandonment); and Mulberry Creek (abandonment).

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Project Study Report	-Caltrans-
Project Report/EIR	\$0
Final Design	\$75,460
ROW	\$11,280
Construction	\$893,400
Total	\$980,140

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Measure I	\$734,571
State STIP	\$72,889
State STIP-CRRSAA	\$11,949
State STP	\$36,000
TCEP	\$75,000
LPP Formula	\$12,731
CMAQ	\$7,000
TBD	\$30,000
Total	\$980,140

Board Approved Funding: \$980,140,000

Lead Agency: SBCTA


Project Manager: Heng Chow (909) 884-8276
hchow@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

SAN BERNARDINO COUNTY TRANSPORTATION AUTHORITY
PROJECT DELIVERY – KRISTI HARRIS, DIRECTOR
PROJECT STATUS – SEPTEMBER 2025

I-10 EASTBOUND TRUCK CLIMBING LANE

Map of Project:

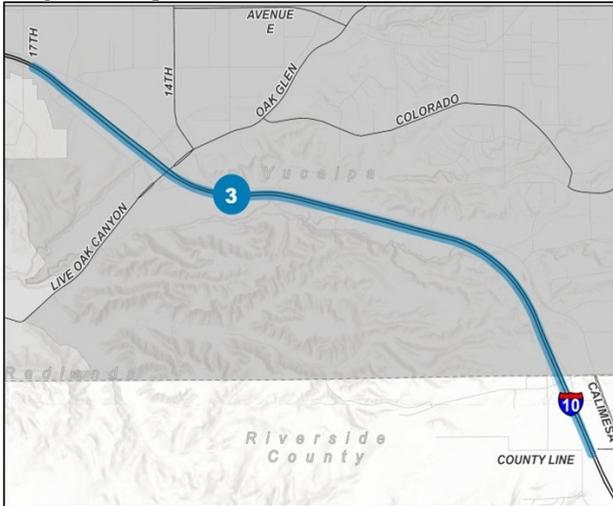

Project Scope Summary:

This project will add a truck climbing lane from west of the 16th Street Bridge in the City of Yucaipa to just east of the County Line Road Bridge at the San Bernardino County and Riverside County line.

Project Benefit:

The addition of a truck climbing lane will separate slow moving trucks that are climbing the steep grade along the project from the general traffic lanes.

Project Status and Continuing Activities:

- The construction contract was awarded in December 2023.
- The Notice to Proceed (NTP) was issued in March 2024.
- Project construction was completed in August 2025 and a Ribbon Cutting Ceremony was held in the City of Yucaipa
- Final operational and safety inspections by Caltrans and other closeout activities are ongoing.

Project Notes of Interest:

- The project will use \$2.9M of STIP/RIP funds for the final design phase. Approximately \$24M of State Transportation Corridor Enhancement Program (TCEP) funds were awarded for the construction phase of the project.
- The project is being designed to integrate with a recent State Highway Operations and Protection Program (SHOPP) pavement rehabilitation project that was just completed. Coordination between both projects led to an estimated overall cost savings from the initial concept estimate of \$45 million.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Oct 2015
Project Initiation Document (PID) Approved	Jun 2017
Environmental Clearance (PA/ED)	Nov 2020
Final Design Approved (RTL)	Nov 2022
Construction Notice to Proceed	Mar 2024
Complete for Beneficial Use	Jun 2025
End of Project	[May 2026]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Project Report and Env Document	\$2,537
Final Design	\$3,438
ROW	N/A
Construction Capital	\$33,180
Total	\$39,155

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
State-TCEP Delivery Plan	\$24,864
Measure I	\$11,394
State - STIP/RIP	\$2,890
TBD	\$7
Total	\$39,155

Board Approved Funding: \$39,148,000


Lead Agency: SBCTA

Project Manager: Paul Melocoton (909) 884-8276
pmelocoton@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

SR-210 LANE ADDITION – HIGHLAND AVENUE TO SAN BERNARDINO AVENUE

Map of Project:

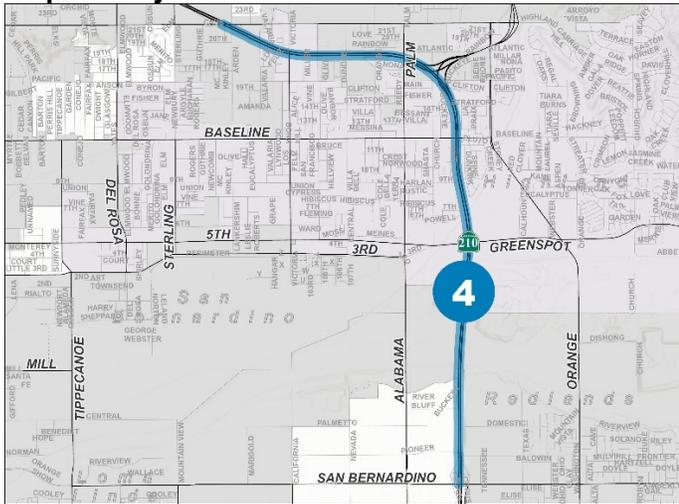

Project Scope Summary:

This gap closure project included the addition of one general purpose lane in each direction within the median of SR-210 generally between Highland Avenue in the City of San Bernardino and San Bernardino Avenue in the City of Redlands. Pavement rehabilitation (rehab) work also occurred along this section of the corridor in select locations.

Project Benefit:

The improvements will decrease congestion during peak traffic periods and improve traffic operations with elimination of the lane drop in each direction. The project also replaced existing asphalt pavement with longer life concrete pavement and replaced pavement sections in poor condition.

Project Status and Continuing Activities:

- The Construction contract was awarded by the SBCTA Board in November 2019.
- Construction began in February 2020 and achieved Complete for Beneficial Use in June 2023.
- Construction is 100% complete through December 2023 and relief of maintenance was issued January 2024. All of the mainline widening is complete.
- Project has entered a 4-year landscape maintenance period to be completed fall 2027.

Project Notes of Interest:

- As the SR-210 Lane Addition and SR-210 Base Line Interchange projects align geographically and share similar delivery schedules, they were combined for the design, right-of-way, and construction phases to minimize cost and schedule.
- Caltrans pavement rehab work was added to this project's scope and funding (SHOPP) which included new concrete pavement between 5th Street and Lugonia Avenue.

Lead Agency: SBCTA

Project Manager: Juan Lizarde (909) 884-8276
jlizarde@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	2011
Project Initiation Document (PID) Approved (by Caltrans)	May 2008
Environmental Clearance (PA/ED)	Jan 2017
Final Design Approved (RTL)	Apr 2019
Construction Notice to Proceed	Feb 2020
Complete for Beneficial Use	June 2023
End of Project	[Feb 2028]


Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Study Report	Caltrans
Project Report	\$3,393
Final Design	\$12,856
ROW	\$5,699
Construction	\$141,642
Total	\$163,590

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
State SHOPP	\$42,121
State STIP/RIP	\$25,000
Measure I	\$122,255
TBD	\$(25,789)
Total	\$163,590

Board Approved Funding: \$189,376,000

I-15 CORRIDOR FREIGHT AND EXPRESS LANES PROJECT (Contract 1)

Map of Project:

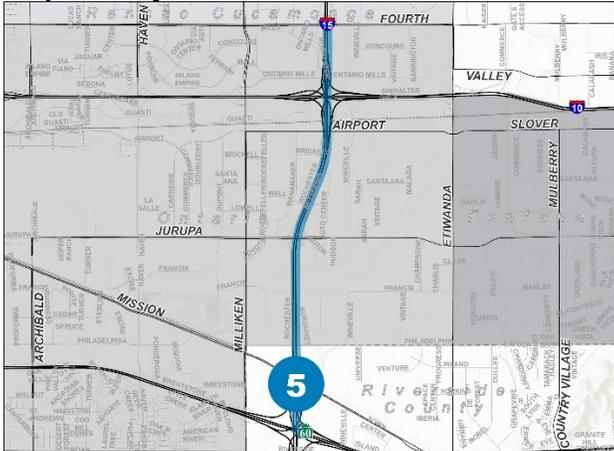

Project Scope Summary:

Addition of auxiliary lanes to improve freight corridor movement and addition of two express lanes in each direction on the I-15 from south of SR-60 to about Foothill Boulevard.

Project Benefit:

Improve freight corridor movement and provide reliable travel times, manage traffic, and increase capacity.

Project Status and Continuing Activities:

- Coordination with Brightline West High Speed Rail is ongoing from Rochester Overhead to Etiwanda Undercrossing to ensure project compatibility with Contract 1.
- The construction contract was awarded in November 2024.
- The Notice to Proceed (NTP) was issued in February 2025, and construction is now underway.

Project Notes of Interest:

- SBCTA received \$119 million in Trade Corridor Enhancement Program (TCEP) grant funds in December 2020.
- Full funding plan based on 10 Year Delivery Plan approved by the Board in December 2021.
- SBCTA received \$52 million in supplemental TCEP funds in October 2024.

Schedule Summary

Milestone	Actual [Forecast]
Start of Project	Oct 2012
Project Initiation Document (PID)	Sept 2014
Environmental Clearance (PA/ED)	Dec 2018
Final Design Approved (RTL)	Oct 2023
Construction NTP	Feb 2025
Complete for Beneficial Use	[July 2028]
End of Project	[Dec 2031]

Budgetary Estimate At Completion (\$000's)

Cost Item	Amount
Project Report and Env Document	\$12,465
Final Design	\$30,250
ROW	\$603
Construction	\$494,077
Total	\$537,395

Funding Estimate At Completion (\$000's)

Funding Source	Amount
Measure I	\$199,471
TCEP	\$170,390
STIP/RIP	\$72,274
LPP (Formula) SB1	\$11,554
CMAQ	\$44,537
HIP	\$2,506
STP	\$38,966
TBD	(\$2,303)
Total	\$537,395

Board Approved Funding: \$539,698,000

Lead Agency: SBCTA

Project Manager: David Tan
(909) 884-8276
dtan@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

I-215 BI-COUNTY / SEGMENT 5 LANDSCAPING

Map of Project:



Project Scope Summary:

This project provides landscaping on Interstate 215 from Orange Show Road to the San Bernardino County/Riverside County line (Bi-County), and from Massachusetts Avenue to the SR-210/I-215 Interchange (Segment-5).

Project Status and Continuing Activities:

- Environmental Clearance was approved in June 2020.
- The 100% Plans, Specifications and Estimate were approved in July 2025.
- The project acquired an easement from a private property for irrigation purposes.
- Federal Authorization (E-76) was issued in August 2025.
- An Invitation for Bid (IFB) for construction services was released on September 3, 2025. Contract award is scheduled for December 2025.

Project Notes of Interest:

- The HOV lanes are complete and were opened to traffic in late 2015. This project is a follow-up landscaping project for the corridor.
- Proposed landscaping includes the use of drought tolerant, California-friendly and low maintenance trees and shrubs, as well as inert materials such as decomposed granite, gravel mulch, rock blanket, and boulders.
- The landscape construction will be followed by a 1-year Plant Establishment period and a 4-year Establish Existing Planting phase.
- Landscape construction phase estimate escalated at 4% per year to midpoint of construction based on latest escalation analysis.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Jan 2019
Project Initiation Document (PID) Approved	-incl. in PA/ED-
Environmental Clearance (PA/ED)	Jun 2020
Final Design Approved (RTL)	Jul 2025
Construction Notice to Proceed	[Mar 2026]
Complete for Beneficial Use	[Mar 2027]
End of Project	[Jun 2032]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Project Report and Env Document	\$717
Final Design	\$1,813
ROW	\$26
Construction	\$15,942
Total	\$18,498

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Measure I	\$12,875
STP	\$6,717
PNRS	\$623
TBD	\$(1,717)
Total	\$18,498

Board Approved Funding: \$18,500,000


Lead Agency: SBCTA

Project Manager: Juan Lizarde (909) 884-8276
jlizarde@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

I-215 WIDENING – SEGMENT 2 LANDSCAPE

Map of Project:

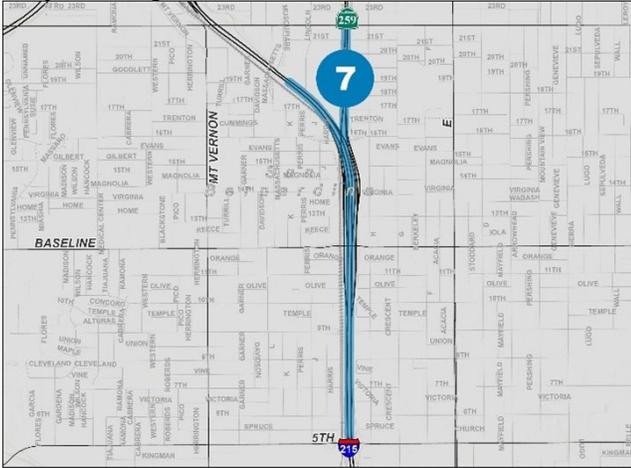

Project Scope Summary:

Project involves landscape replacement in the City of San Bernardino along I-215 from the 5th Street Overcrossing to Muscupiabe Drive and along SR-259 from Baseline Street to Highland Avenue.

Project Status and Continuing Activities:

- Project was advertised for landscape construction services in September 2018 and the Construction contract was awarded in December 2018.
- Construction and installation of landscaping was completed in February 2020, and the one-year plant establishment was completed in December 2020.
- The project has completed the four-year establish existing planting phase, in January 2025, and closeout activities are underway.

Project Notes of Interest:

- Landscaping design utilizes gravel mulch, boulders and drought tolerant, low maintenance plant material and palm trees irrigated with drip and bubbler systems to minimize water use.
- Estimate at completion is below the Board approved cooperative agreement funding due to lower bid results.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Jan 2012
Environmental Clearance (PA/ED)	Nov 2012
Final Design Approved (RTL)	Jan 2017
Construction Notice to Proceed	Jan 2019
Complete for Beneficial Use	Feb 2020
End of Project	[Dec 2025]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
PA/ED	\$35
Final Design	\$660
Construction	\$5,306
Total	\$6,001

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Federal - PNRS	\$4,574
Measure I	\$2,677
TBD	\$(1,250)
Total	\$6,001

Board Approved Funding: \$7,251,000

Lead Agency: Caltrans – Landscape Design
SBCTA – Landscape Construction

Project Manager: Juan Lizarde (909) 884-8276
jlizarde@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

US-395 WIDENING PROJECT – PHASE 2

Map of Project:



Project Scope Summary:

Widen US-395 between 0.4 miles north of Interstate 15 (I-15) and State Route 18 (SR-18 / Palmdale Road), a distance of approximately 7 miles, from two lanes to four lanes. Install continuous raised median, turn lanes and signal modification at various intersections within the project limits.

Project Benefit:

The project will relieve congestion and enhance the operational efficiency of US-395.

Project Status and Continuing Activities:

- The Construction Management contract was awarded in December 2024.
- The project achieved the Ready to List milestone in June 2025.
- Acquisition of Right-of-Way is complete.
- An Invitation for Bid (IFB) for construction services is expected to be released in the Fall of 2025.

Project Notes of Interest:

- This “gap closure” Project is the second phase of a three-phase project between I-15 and Desert Flower Road. Construction is complete for Phase 1, between SR-18 and Chamberlaine Way. Phase 3 between Chamberlaine Way and Desert Flower Road will be completed as funding becomes available.
- SBCTA will receive \$7.65 million in SHOPP funds for construction capital, from Caltrans.
- SBCTA received \$30 million in Trade Corridor Enhancement Program (TCEP) grant funds in June 2023.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Jul 2002
Project Initiation Document (PID)	Aug 2005
Environmental Clearance (PA/ED)	Dec 2009
Final Design Approved (RTL)	June 2025
Construction Notice to Proceed	[Nov 2025]
Complete for Beneficial Use	[March 2028]
End of Project	[Sept 2028]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Final Design	\$9,234
ROW	\$24,449
Construction	\$88,266
Total	\$121,949

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Federal - STP	\$33,997
Federal Earmark	\$2,000
State - SHOPP	\$7,652
Measure I	\$18,673
CRRSAA	\$9,961
TCEP	\$30,000
TBD	\$19,666
Total	\$121,949

Board Approved Funding: \$102,283,000


Lead Agency: SBCTA – Right of Way
SBCTA – Construction
SBCTA – Design

Project Manager: David Tan (909) 884-8276
dtan@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

SR-62 / SAGE TO AIRWAY AVENUE

Map of Project:

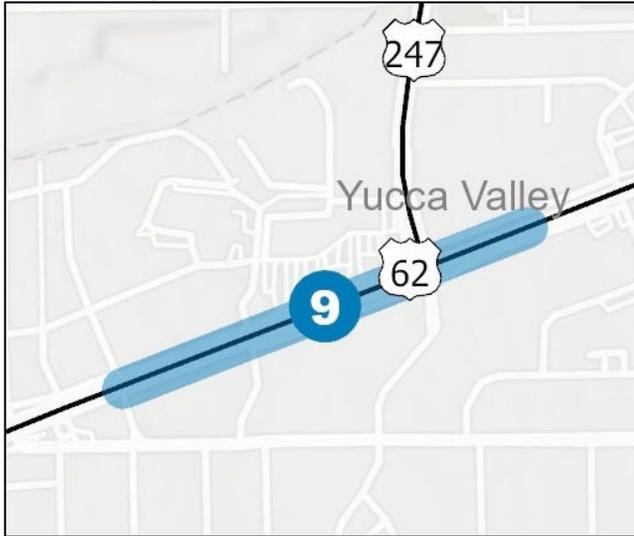

Project Scope Summary:

The project will address traffic congestion along an approximately one mile stretch of State Route 62 (SR-62) along the commercial sector of the Town of Yucca Valley

Project Benefit:

The project will improve vehicular throughput and traffic operations by improving up to five roadway intersections and evaluating needed traffic improvements from Sage Avenue to Airway Avenue. The project will also provide standard roadway shoulders and improve pedestrian and bicycle features.

Project Status and Continuing Activities:

- An engineering consultant was awarded a professional design service contract in October 2025
- The project delivery process will begin with the Project Initiation Document (PID) Phase which will evaluate various conceptual solutions to address traffic operational needs.

Project Notes of Interest:

- Incorporation of Smart Corridor elements are being evaluated for this project.
- Project improvements will consider SBCTA’s Cajon Pass Emergency Bypass strategies

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Aug 2025
Project Initiation Document (PID) Approved	Oct 2026
Environmental Clearance (PA/ED)	Nov 2028
Final Design Approved (RTL)	TBD
Construction Notice to Proceed	TBD
Complete for Beneficial Use	TBD
End of Project	TBD

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Project Report and Env Document	\$2,623
Final Design	\$TBD
ROW/Utilities Capital	\$TBD
Construction	\$TBD
Total	\$2,623

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Measure I	\$2,423
Town of Yucca Valley DIF	\$200
Total	\$2,623

Board Approved Funding: \$xxx


Lead Agency: SBCTA

Project Manager: Paul Melocoton (909) 884-8276
pmelocoton@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

SR-18 MEDIAN WIDENING AND REPROFILING PROJECT

Map of Project:

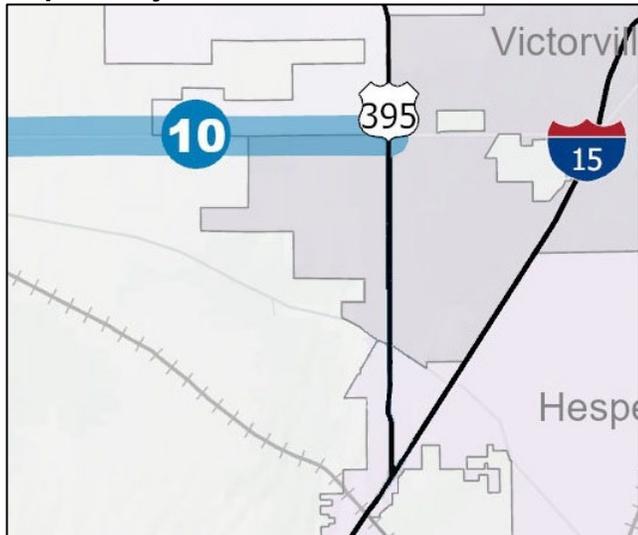

Project Scope Summary:

Addition of a center median separating eastbound and westbound lanes to improve safety and operations and reduce delays from the County line to US 395. Reprofile SR-18 mainline to enhance ride quality.

Project Benefit:

Enhance safety, reduce congestion, support economic and environmental benefits, strengthen regional resiliency during emergencies, and improve multimodal access through complete street features.

Project Status and Continuing Activities:

- The Project Study Report was approved in June 2025.
- The PA/ED contract was awarded in September 2025.
- Preliminary design and environmental studies are underway.

Project Notes of Interest:

- Funding for the project is presently programmed only through the PA/ED phase.
- Construction phase estimate escalated at 4% per year to midpoint of construction based on latest escalation analysis.

Schedule Summary

Milestone	Actual [Forecast]
Start of Project	Apr 2021
Project Initiation Document (PID)	June 2025
Environmental Clearance (PA/ED)	[June 2027]
Final Design Approved (RTL)	[Sept 2029]
Construction NTP	[Apr 2030]
Complete for Beneficial Use	[Oct 2032]
End of Project	[Apr 2033]

Budgetary Estimate At Completion (\$000's)

Cost Item	Amount
Project Report and Env Document	\$8,217
Final Design	
ROW	
Construction	
Total	\$8,217

Funding Estimate At Completion (\$000's)

Funding Source	Amount
Measure I	\$8,217
Total	\$8,217

2025 10-Year Delivery Plan: \$12,000,000

Lead Agency: SBCTA

Project Manager: David Tan
(909) 884-8276
dtan@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

I-15 / CAJON PASS NORTHBOUND TRUCK CLIMBING LANE EXTENSION

Map of Project:



Project Scope Summary:

The project will extend the existing truck lane in the northbound direction from 2.7 miles north of Kenwood Avenue, for approximately 3.4 miles to State Route 138.

Project Benefit:

This project will improve operations by eliminating the drop lane and allowing for continuous traffic flow by separating slower moving vehicles from the general-purpose lanes.

Project Status and Continuing Activities:

- SBCTA awarded a combined PID & PA/ED design contract in July 2025.
- SBCTA conducted biological survey's summer 2025.
- The anticipated Environmental Document is an Initial Study/Categorical Exemption (IS/CE).

Project Notes of Interest:

- The Projects outside widening will also accommodate any future express lanes along the corridor.
- Close coordination is being conducted with the Brightline West Project which will have median improvements along the corridor.
- SBCTA is working to obtain TCEP Funds for the Project.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Oct 2024
Project Initiation Document (PID) Approved	[Mar 2026]
Environmental Clearance (PA/ED)	[Dec 2026]
Final Design Approved (RTL)	[May 2028]
Construction Notice to Proceed	[Nov 2028]
Complete for Beneficial Use	[Jun 2031]
End of Project	[Jun 2032]

Lead Agency:

SBCTA

Project Manager:

Juan Lizarde (909) 884-8276
jlizarde@gosbcta.com

Public/Media Contact:

Tim Watkins (909) 884-8276
twatkins@gosbcta.com

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Study Report/PA/ED	\$6,250
Final Design	\$5,000
ROW	\$0
Construction	\$99,750
Total	\$111,000

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Measure I	\$60,000
TBD	\$51,000
Total	\$111,000

Board Approved Funding: \$60,000,000

SR-60 / CENTRAL AVENUE

Map of Project:



Project Scope Summary:

The project will widen the Central Avenue bridge over SR 60 in the City of Chino, widen the freeway ramps, and improve ramp intersections.

Project Benefit:

The project will provide additional left turn storage for vehicles entering the freeway from Central Avenue and improve traffic flow across the SR-60/Central Avenue Bridge. The project will also provide standard roadway shoulders, and improve pedestrian and bicycle features.

Project Status and Continuing Activities:

- A project completion celebration was held at the Chino City Hall on September 5, 2024.
- Caltrans issued the partial Relief from Maintenance to SBCTA
- A contract was awarded to a landscape contractor to perform the four-year Establish Existing Planting (EEP) phase.
- EEP phase will began in June 2025.

Project Notes of Interest:

- Replacement landscaping will be added including a one year plant establishment period and a four-year establish existing planting landscape maintenance period.
- The California Transportation Commission (CTC) allocated over \$8.6 million in available State Proposition 1B TCIF funding for the project in June 2020.

Lead Agency: SBCTA

Project Manager: Paul Melocoton (909) 884-8276
pmelocoton@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

Schedule Summary

Milestone	Actual [Forecast]
Start of Project	June 2014
Project Initiation Document (PID) Approved	Aug 2016
Environmental Clearance (PA/ED)	Jan 2018
Final Design Approved (RTL)	Jun 2020
Construction Notice to Proceed	Jan 2021
Complete for Beneficial Use	Mar 2024
End of Project	[Dec 2029]

Budgetary Estimate At Completion (\$ 000's)

Cost Item	Amount
Project Report and Env Document	\$1,294
Final Design	\$2,162
ROW/Utilities Capital	\$866
Construction	\$34,291
Total	\$38,613

Funding Estimate At Completion (\$ 000's)

Funding Source	Amount
Measure I	\$11,395
City of Chino DIF	\$16,927
State - TCIF	\$8,638
TBD	\$1,653
Total	\$38,613

Board Approved Funding: \$36,960,000

I-10 / CEDAR AVENUE

Map of Project:



Project Scope Summary:

Reconstruction of the interchange includes widening the I-10 overcrossing, replacement of the railroad bridge, roadway improvements along Cedar Avenue from Bloomington Avenue to Slover Avenue, and adding capacity to the ramps.

Project Benefit:

The improvements will decrease congestion and improve traffic operations.

Project Status and Continuing Activities:

- The construction contract was awarded in October 2022.
- The construction work started in January 2023.
- The construction of retaining walls, interchange ramp improvements, Cedar overcrossing bridge widening, and Cedar railroad overhead bridge are in progress.

Project Notes of Interest:

- This project is the number 1 priority project in the Measure I 2010-2040 Freeway Interchange Program.
- The Cooperative Agreement for PS&E between the County and SBCTA was executed in February 2018 with County leading the PS&E phase, SBCTA being the Project Manager, and Caltrans executing the design.
- The Cooperative Agreement for the ROW and Construction phases was executed in January 2019 designating SBCTA as lead agency for these phases.
- The project has a landscaping component that will be followed by 1-year Plant Establishment and 2-year Establish Existing Planting.

Lead Agency: County of San Bernardino (PS&E)
SBCTA (ROW and Construction)

Project Manager: Heng Chow (909) 884-8276
hchow@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	2001
Project Initiation Document (PID) Approved (by others)	Nov 2001
Environmental Clearance (PA/ED)	Jul 2013
Ready to List (RTL)	Jun 2022
Construction Notice to Proceed	Jan 2023
Complete for Beneficial Use	[July 2026]
End of Project	[Dec 2029]


Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Study Report	County
Project Report	\$559
Final Design	\$9,109
ROW	\$7,470
Construction	\$99,647
Total	\$116,785

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Federal - STP	\$4,680
Federal - HIP	\$3,552
Measure I	\$71,087
CPUC	\$5,000
County of San Bernardino DIF	\$28,349
TBD	\$4,117
Total	\$116,785

Board Approved Funding: \$112,668,000

I-10 / MOUNT VERNON AVENUE

Map of Project:

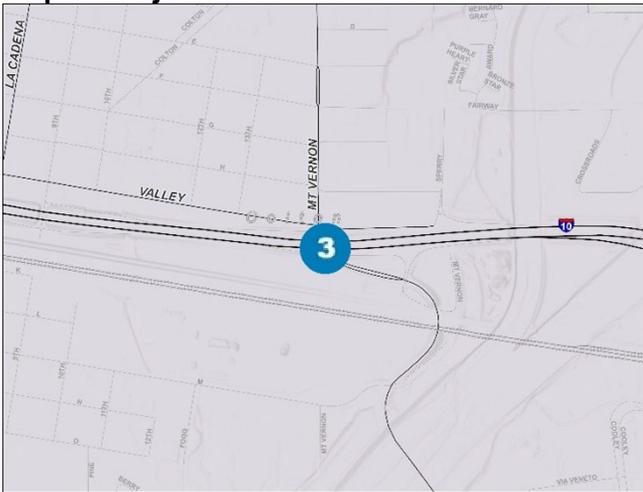

Project Scope Summary:

The project will replace the existing Mount Vernon Avenue bridge over I-10 and provide local circulation improvements in the City of Colton.

Project Benefit:

This project will make operational and safety improvements which will reduce local traffic congestion along Mount Vernon Avenue at the I-10 interchange. In addition, the bridge will be lengthened to accommodate future I-10 Express Lanes.

Project Status and Continuing Activities:

- Project Development Team (PDT) meetings for the PA/ED phase began in January 2019.
- Caltrans determined that an Initial Study/Mitigated Negative Declaration (IS/MND) was the appropriate Environmental Document for project approval.
- Geometric Approval Drawings (GAD's) were approved by Caltrans in March 2021.
- Circulation of the DED for public review and comment along with a public hearing occurred in July, 2021.
- The Final Environmental Document (FED) was approved by Caltrans in March, 2022 and the Final Project Report was approved by Caltrans in April, 2022.
- A Construction Management contract was awarded in June 2023.
- Final Design approval was achieved in August, 2025. Contract award is scheduled for January 2026.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Jan 2016
Project Initiation Document (PID) Approved	Dec 2018
Environmental Clearance (PA/ED)	Apr 2022
Final Design Approved (RTL)	Aug 2025
Construction Notice to Proceed	[Jan 2026]
Complete for Beneficial Use	[Aug 2028]
End of Project	[Apr 2032]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Study Report/PA/ED	\$2,742
Final Design	\$3,124
ROW	\$5,455
Construction	\$91,962
Total	\$103,283

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Measure I	\$92,516
City of Colton DIF	\$4,971
TBD	\$5,796
Total	\$103,283

Board Approved Funding: \$97,487,000

Project Notes of Interest:

- The intersection of Mount Vernon Avenue and East Valley View Boulevard is a five-legged signalized intersection that requires careful consideration to ensure safe and efficient traffic operations.
- Construction phase estimate based on the 100% PS&E submittal and escalated at 4% per year to midpoint of construction based on latest escalation analysis.


Lead Agency: SBCTA

Project Manager: Juan Lizarde (909) 884-8276
jlizarde@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

I-10 / ALABAMA STREET

Map of Project:

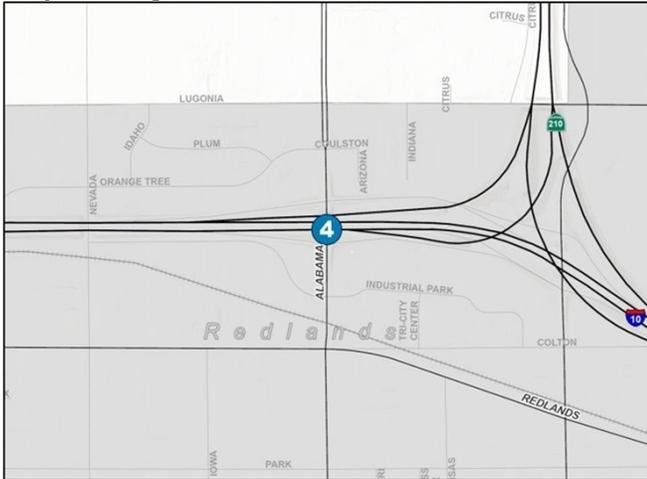

Project Scope Summary:

This project will widen Alabama Street from Orange Tree Lane to Industrial Park Avenue in the City of Redlands. The operational improvements include widening the eastbound and westbound off-ramps at the I-10/Alabama Street Interchange.

Project Benefit:

The project will improve traffic operations and reduce traffic congestion on Alabama Street and at the I-10 interchange.

Project Status and Continuing Activities:

- The construction was completed for beneficial use in December 2022.
- The project received partial Relief of Maintenance from Caltrans in June 2023.
- The one-year Plant Establishment period began in April 2023 and ended in April 2024.
- The Establish Existing Planting (EEP) contract was awarded in April 2024. The 4-year EEP is in progress.

Project Notes of Interest:

- SBCTA is leading the planning, design, ROW, and construction phases per a cooperative agreement with the City of Redlands.
- This project is the sixth highest priority project in the Measure I 2010-2040 Freeway Interchange Program.
- The project has a landscaping component that will be followed by 1-year Plant Establishment and 4-year Establish Existing Planting after complete for beneficial use.
- In an effort to secure additional funding for the project, SBCTA reached out to Caltrans requesting financial contribution from their Minor Program Funds. In November 2019, Caltrans agreed to contribute SHOPP funds of \$1,250,000 towards the eastbound off-ramp widening portion of the project. Caltrans contribution agreement and City cooperative agreement amendment were executed in August 2020.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Feb 2017
Project Initiation Document (PID) Approved	Dec 2017
Environmental Clearance (PA/ED)	Jun 2019
Final Design Approved (RTL)	Jun 2021
Construction Notice to Proceed	Jan 2022
Complete for Beneficial Use	Dec 2022
End of Project	[Aug 2028]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
PA/ED	\$959
Final Design	\$1,097
ROW	\$33
Construction	\$11,478
Total	\$13,567

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Measure I	\$6,745
City of Redlands DIF	\$7,188
Caltrans SHOPP	\$1,250
TBD	\$(1,616)
Total	\$13,567

Board Approved Funding: \$15,183,000


Lead Agency: SBCTA

Project Manager: Heng Chow (909) 884-8276
hchow@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

SR-210 / BASE LINE

Map of Project:

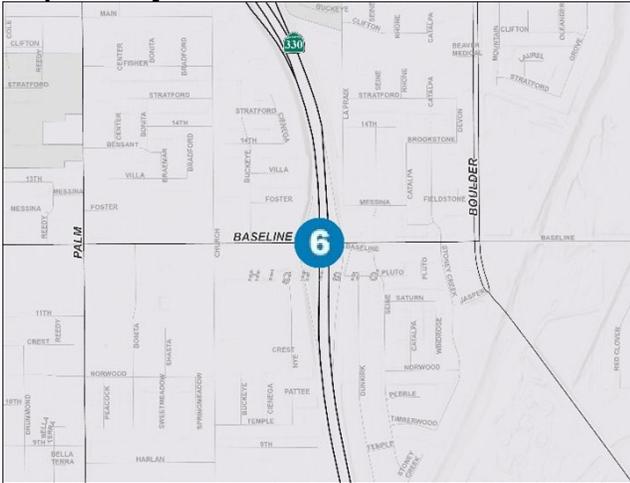

Project Scope Summary:

The project will widen Base Line at the SR-210 Interchange as well as widen the existing westbound on and off-ramps, and eastbound on-ramp to SR-210 in the City of Highland.

Project Benefit:

This project will make operational and safety improvements and reduce local traffic congestion at the SR-210 / Base Line Interchange.

Project Status and Continuing Activities:

- Construction contract awarded by SBCTA Board in November 2019 and the groundbreaking ceremony was held on February 26, 2020.
- Construction began in February 2020 and achieved Complete for Beneficial use in June 2023.
- Bridge widening including sidewalk and concrete barrier work completed. All of the interchange work is complete.
- Project has entered a 4-year landscape maintenance period to be completed fall 2027.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Feb 2013
Project Initiation Document (PID) Approved	N/A
Environmental Clearance (PA/ED)	Dec 2016
Final Design Approved (RTL)	Apr 2019
Construction Notice to Proceed	Feb 2020
Complete for Beneficial Use	June 2023
End of Project	[Feb 2028]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Study Report	\$214
Project Report	\$1,042
Final Design	\$1,499
ROW	\$813
Construction	\$26,893
Total	\$30,461

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Measure I	\$20,143
City of Highland DIF	\$14,870
TBD	\$(4,552)
Total	\$30,461

Board Approved Funding: \$35,013,000

Project Notes of Interest:

- As the SR-210 Base Line Interchange and SR-210 Lane Addition projects align geographically and share similar delivery schedules, they have been combined for the design, right-of-way, and construction phases to minimize cost and schedule.
- Estimate at completion is less than the Board approved funding due to lower bid results.

Lead Agency: SBCTA

Project Manager: Juan Lizarde (909) 884-8276
jlizarde@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com

I-15 AND I-215 INTERCHANGE IMPROVEMENTS (DEVORE)

Map of Project:



Project Scope Summary:

This project reconfigured the interchange to provide four lanes in each direction on I-15. The project also included adding truck bypass lanes and reconnecting Cajon Boulevard.

Project Benefit:

This project reduced congestion at the bottleneck along the I-15 corridor, and improved local circulation through the reconnection of Cajon Boulevard.

Project Status and Continuing Activities:

- Close out cost reconciliation is nearly complete.
- Post project right of way engineering is complete.
- Post construction environmental mitigation is complete.

Project Notes of Interest:

- Project was the first design build project for SBCTA and Caltrans District 8.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	July 2007
Project Initiation Document (PID) Approved	Mar 2009
Environmental Clearance (PA/ED)	Feb 2012
Final Design Approved (RTL)	Jan 2016
Construction Notice to Proceed	Aug 2013
Complete for Beneficial Use	June 2016
End of Project	Aug 2025

Budgetary Estimate at Completion (\$ 000's)	
Cost Item	Amount
Study Report	Incl in PA/ED
Project Report	\$10,295
Preliminary Engineering	\$6,580
ROW	\$41,877
Construction	\$266,253
Total	\$325,005

Funding Estimate at Completion (\$ 000's)	
Funding Source	Amount
Federal - STP	\$65,708
Federal - DEMO	\$2,000
Federal - IMD	\$3,341
State - CMIA	\$53,743
State - SHOPP	\$83,865
State - STIP/RIP	\$45,145
Measure I (2010 - 2040) Cajon	\$53,696
Measure I (Major Projects)	\$10,490
Private Utility Companies	\$7,017
Total	\$325,005

Board Approved Funding: \$325,005,000

Lead Agency:

Caltrans – Design Build
SBCTA - ROW, Utilities, Railroad

Project Manager:


Sal Chavez
(909) 884-8276
schavez@gosbcta.com

Public/Media Contact:

Tim Watkins (909) 884-8276
twatkins@gosbcta.com

I-215 / BARTON ROAD

Map of Project:

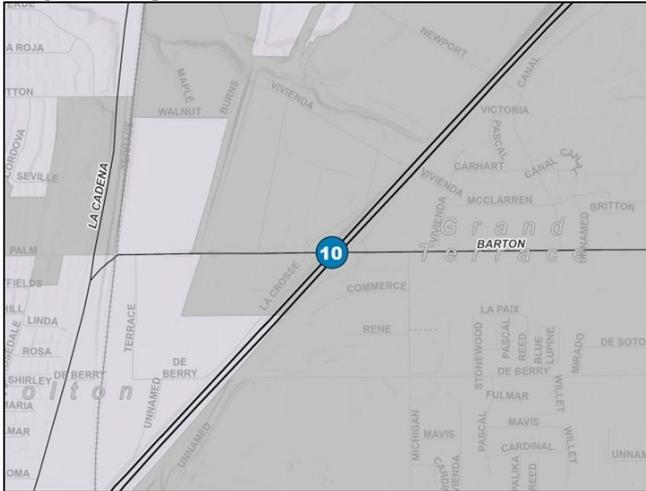

Project Scope Summary:

This project reconstructed the I-215/Barton Road interchange in the City of Grand Terrace. The existing overcrossing was replaced with a new structure with four through lanes and a longer structure to accommodate the ultimate mainline widening. This project also includes the implementation of a roundabout and local circulation improvements.

Project Benefit:

The project improves traffic flow and safety resulting in reduced congestion.

Project Status and Continuing Activities:

- Construction was completed on July 24, 2020 and Relief of Maintenance was granted on August 26, 2020.
- Right-of-way has been conveyed to Caltrans and the City of Grand Terrace.
- Disposal of surplus properties are ongoing.

Project Notes of Interest:

- The project is one of the few statewide pilot projects implementing the Construction Management/General Contractor (CM/GC) delivery method.

Lead Agency:

Caltrans – Design and Construction
SBCTA - Right-Of-Way

Project Manager:

Paul Melocoton (909) 884-8276
pmelocoton@gosbcta.com

Public/Media Contact:

Tim Watkins (909) 884-8276
twatkins@gosbcta.com

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Dec 2007
Environmental Clearance (PA/ED)	Mar 2014
Final Design Approved (RTL)	Apr 2017
Construction Notice to Proceed	Jan 2018
Complete for Beneficial Use	Jul 2020
End of Project	[Dec 2025]


Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Study Report	-Incl in PA/ED-
Project Report	\$2,990
Final Design	\$6,480
ROW	\$35,629
Construction	\$59,874
Totals	\$104,973

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
State – STIP/RIP	\$17,400
Federal - STP	\$16,218
Federal - Section 112 and 115	\$2,482
Federal - DEMO	\$6,481
Federal - EARREPU	\$1,710
Private – Level 3 Communication	\$71
Measure I (2010-2040)	\$61,000
RCTC	\$156
Measure I (1990-2010)	\$2,134
TBD	\$(2,679)
Total	\$104,973

Board Approved Funding: \$107,652,000

I-215 / UNIVERSITY PARKWAY

Map of Project:

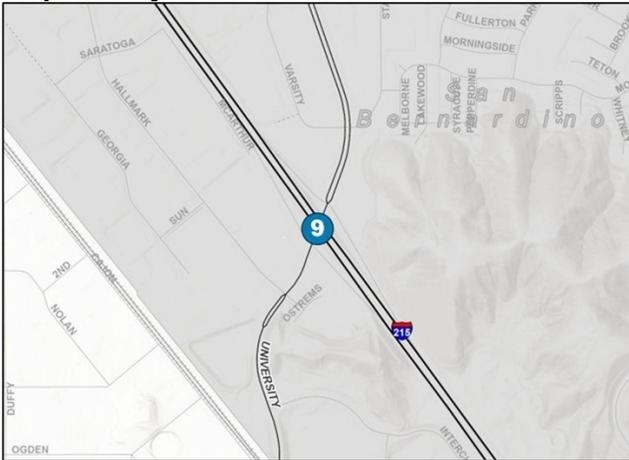

Project Scope Summary:

This project will reconfigure the existing interchange at I-215 and University Parkway to address present congestion and heavy traffic movement through the interchange in the City of San Bernardino.

Project Benefit:

The project will reduce delays and improve freeway access.

Project Status and Continuing Activities:

- Project was advertised on May 15, 2024 and bids were opened on June 4, 2024.
- The construction contract was awarded in September 2024 and work began in December 2024.
- Work is continuing with work along University Avenue.
- Work is continuing on the establishment of the notification system for information and alerts during construction.

Project Notes of Interest:

- A new interchange configuration called the Diverging Diamond Interchange (DDI) configuration was determined to be a feasible interchange configuration for the project with anticipated reduced right-of-way impacts and lower construction costs than other alternatives.
- This project includes a one-year Plant Establishment period for maintenance of newly planted trees.

Lead Agency: SBCTA

Project Manager: Paul Melocoton (909) 884-8276
 pmelocoton@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
 twatkins@gosbcta.com

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Nov 2015
Project Initiation Document (PID) Approved	Oct 2016
Environmental Clearance (PA/ED)	Jul 2020
Final Design Approved (RTL)	Mar 2024
Construction Notice to Proceed	Dec 2024
Complete for Beneficial Use	[Apr 2026]
End of Project	[Dec 2027]


Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Project Report	\$1,530
Final Design	\$1,297
ROW	\$2,296
Construction	\$20,697
Totals	\$25,820

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Federal – STP/HIP	\$5,000
Federal - DEMO	\$735
Measure I	\$16,437
City of San Bernardino DIF	\$3,645
TBD	\$3
Total	\$25,820

Board Approved Funding: \$25,817,000

SR-210 / WATERMAN AVENUE (SR-18)

Map of Project:

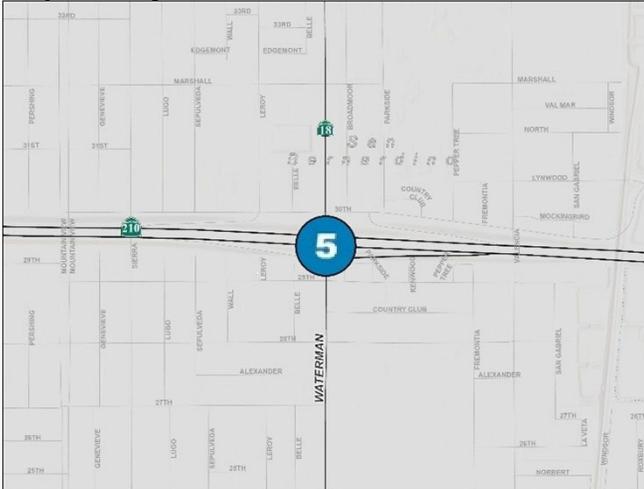

Project Scope Summary:

The project will improve the SR-210 Waterman Avenue Interchange in the City of San Bernardino by widening the eastbound on-ramp to two lanes and restriping the Waterman Avenue Overcrossing to provide dual left-turn lanes in each direction.

Project Benefit:

This project will improve traffic operations and reduce local traffic congestion on Waterman Avenue and the eastbound entrance ramp to the SR-210 Freeway.

Project Status and Continuing Activities:

- The Contract was awarded on July 3, 2024.
- Work began on January 6, 2025.
- Work is continuing with completion of the bridge deck resurfacing and installation of electrical components and signals
- The notification system for information and alerts during construction has been established.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Dec 2021
Environmental Clearance (PA/ED)	Jul 2023
Final Design Approved (RTL)	May 2024
Construction Notice to Proceed	Nov 2024
Complete for Beneficial Use	[Nov 2025]
End of Project	[Sep 2027]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Study Report/PA/ED	\$292
Final Design	\$573
Construction	\$9,300
Total	\$10,165

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Measure I	\$7,861
City of San Bernardino DIF	\$1,949
TBD	\$355
Total	\$10,165

Board Approved Funding: \$9,810,000

Project Notes of Interest:

- This project is in the SBCTA interchange phasing program and is the first phase in other improvements to the SR-210 Waterman Avenue Interchange.
- This project includes a one-year Plant Establishment period for maintenance of newly planted trees.

Lead Agency: SBCTA

Project Manager: Paul Melocoton (909) 884-8276
 pmelocoton@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
 twatkins@gosbcta.com

MONTE VISTA AVENUE AND UNION PACIFIC RAILROAD

Map of Project:



Project Scope Summary:

This project will bridge Monte Vista Avenue in the City of Montclair over the existing Union Pacific Railroad (UPRR) and State Street.

Project Benefit:

This project will improve traffic operations, local circulation, air quality, and safety by eliminating the at-grade crossing between Monte Vista Avenue and UPRR.

Project Status and Continuing Activities:

- Final design and right-of-way phase activities were completed and led by the City of Montclair.
- A contract for construction services was approved by the SBCTA Board of Directors in July 2017.
- Relief of maintenance was issued February 2020.
- Project close-out efforts are underway including claims resolution, final billings and cost reconciliation.

Project Notes of Interest:

- A groundbreaking ceremony was held in October 2017.
- Ribbon cutting ceremony was held on September 23, 2019 and the new bridge was open to traffic.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Apr 2001
Project Initiation Document (PID) Approved (by others)	N/A
Environmental Clearance (PA/ED)	July 2013
Final Design Approved (RTL)	July 2016
Construction Notice to Proceed	Aug 2017
Complete for Beneficial Use	Sep 2019
End of Project	[Mar 2026]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Project Report	City
Final Design	City
ROW	City
Construction	\$27,403
Total	\$27,403

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Federal – PNRS	\$10,661
State – TCIF	\$1,019
Measure I	\$7,234
City of Montclair DIF	\$2,435
UPRR	\$1,078
PUC Section 190	\$5,002
TBD	\$(26)
Total	\$27,403

Board Approved Funding: \$27,429,000

Lead Agency:

City of Montclair – Design/ROW
SBCTA – Construction

Project Manager:


Juan Lizarde (909) 884-8276
hstultz@gosbcta.com

Public/Media Contact:

Tim Watkins (909) 884-8276
twatkins@gosbcta.com

MOUNT VERNON AVENUE VIADUCT

Map of Project:

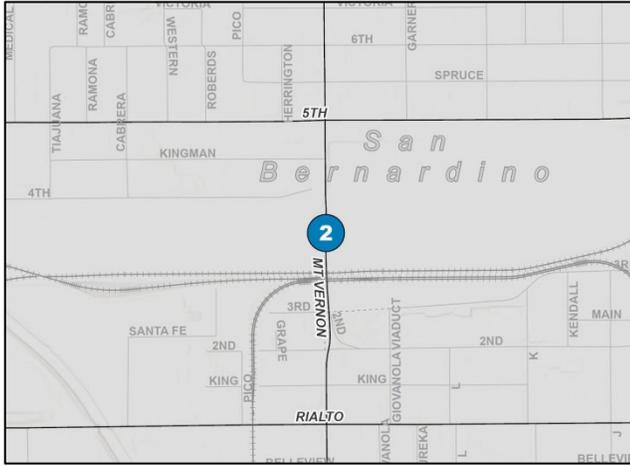

Project Scope Summary:

This project will reconstruct the Mount Vernon Avenue Viaduct over the BNSF Railway intermodal yard in the City of San Bernardino.

Project Benefit:

This project will improve safety by replacing the existing bridge with a new wider and longer bridge.

Project Status and Continuing Activities:

- BNSF mitigation work was completed in December 2023.
- NTP 3 work began in January 2023.
- Utility relocation work is complete.
- The new bridge was completed and opened to traffic in August 2025.

Project Notes of Interest:

- SBCTA is leading the design, right-of-way, and construction phases.
- Cost estimate based on design build contract and estimated final right-of-way and utility relocation costs.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Aug 2009
Project Initiation Document (PID) Approved	N/A
Environmental Clearance (PA/ED)	Jun 2011
Design NTP	Jun 2020
Construction Notice to Proceed	Dec 2020
Complete for Beneficial Use	Aug 2025
End of Project	[Jul 2026]

Lead Agency: SBCTA
Project Manager: David Tan
(909) 884-8276
dtan@gosbcta.com

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Project Report/PA&ED	\$23,118
ROW	\$72,245
Construction	\$149,448
Total	\$244,811


Public/Media Contact: Tim Watkins
(909) 884-8276
twatkins@gosbcta.com

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Federal - HBP	\$149,118
Federal - HIP	\$23,495
Measure I – City Arterial	\$24,840
City of San Bernardino DIF	\$14,405
BNSF	\$29,500
Prop 1B	\$3,453
Total	\$244,811

Board approved funding: \$244,811,000

NORTH FIRST AVENUE BRIDGE OVER BNSF RAILROAD PROJECT

Map of Project:

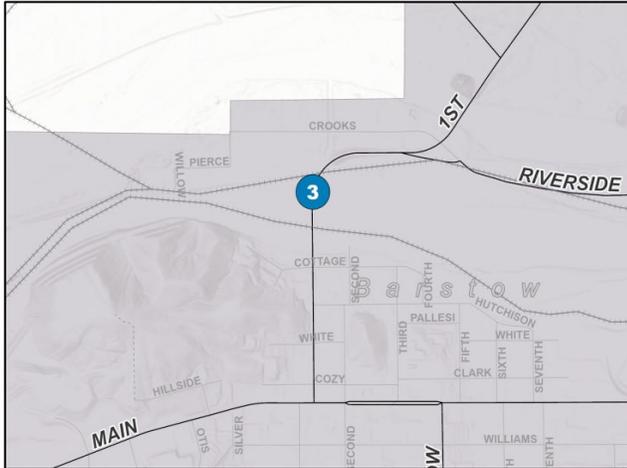

Project Scope Summary:

Replace the existing North First Avenue bridge over a BNSF railyard in the City of Barstow. The bridge was built around 1930 and has been deemed structurally deficient and functionally obsolete. The project includes the construction of new approach roadways, a new 2-lane structure, and the demolition of the old structure once the new facility has been opened to traffic.

Project Benefit:

The replacement of a structurally deficient bridge with a new structure will provide safety benefits and accommodate all legal truck and permit vehicles, provide standard 8-foot shoulder widths, and one 8-foot sidewalk.

Project Status and Continuing Activities:

- The new bridge was completed and opened to traffic in July 2024.
- The construction was completed in December 2024
- Closeout activities are currently in progress.

Project Notes of Interest:

- This project is funded by Federal Highway Bridge Program (HBP) funds, other federal and state funds, and Measure I Major Local Highway Programs funds and City of Barstow funds.
- City of Barstow and SBCTA are working with Caltrans Local Assistance and the HBP program to confirm available HBP project funding.
- City of Barstow was successful in its obtaining \$5 million in CPUC Section 190 funds for the project. An agreement between the City and the CPUC has been executed for this project.
- During the Bridge Inspection Report prepared by Caltrans in April 2012, the bridge Sufficiency Rating (SR) was 3 out of 100. The existing bridge is considered Structurally Deficient (SD) in its superstructure, substructure, and the overall structural evaluation. The existing bridge is also considered Functionally Obsolete (FO) due to its overall geometry and substandard vertical clearance.

- **Lead Agency:** City of Barstow – Environmental, Design and Right of Way
SBCTA – Construction
- **Project Manager:** David Tan (909) 884-8276
dtan@gosbcta.com
- **Public/Media Contact:** Tim Watkins (909) 884-8276
twatkins@gosbcta.com

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	2012
Project Initiation Document (PID)	Mar 2013
Environmental Clearance (PA/ED)	Sep 2016
Final Design Approved (RTL)	Mar 2022
Construction Notice to Proceed	Jan 2023
Complete for Beneficial Use	Aug 2024
End of Project	[Oct 2026]


Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Project Report and Env Doc	\$3,000
Final Design	\$4,635
ROW	\$15,025
Construction	\$49,300
Total	\$71,960

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Federal - HBP	\$70,388
Measure I - MLHP	\$5,670
Local Funds	\$1,155
LSSRP Bond	\$305
Federal - Earmark	\$2,591
CPUC Section 190	\$5,000
TBD	(\$13,149)
Total	\$71,960

Board Approved Funding: \$85,109,000

METROLINK ATP (Phase II)

Map of Project:

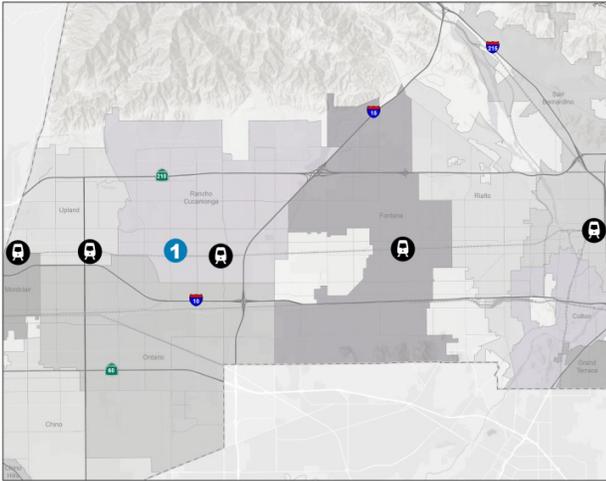

Project Scope Summary:

This project will provide safe pedestrian and bicycle access to key corridors at Metrolink stations in the Cities of Montclair, Upland, Rancho Cucamonga, Fontana, and San Bernardino.

Project Benefit:

This project improves pedestrian and bicycle access and safety with the incorporation of way finding signage, sidewalks, curb ramps, class II bike lanes, high-visibility crosswalks, bicycle parking and signalized crossings.

Project Status and Continuing Activities:

- Phase I work was completed in early March 2019 and project close out is complete.
- Phase II design RFP was released July 2020, and the design contract was awarded in December 2020.
- Request for Design Modification was submitted to Caltrans and approved in November 2022.
- Environmental revalidation was also completed in December 2022 to cover minor scope changes from the original environmental clearance.
- Final 100% Plans, Specifications, and Estimate (PS&E) package completed January 2023. Release of Invitation for Bid occurred in August 2023 and Construction Contract Awarded in February 2024.
- Construction began July 2024 and was completed in April 2025.
- The City of Montclair is separately delivering improvements on Fremont Avenue and Arrow Highway, targeting completion by October 2026.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Aug 2019
Project Initiation Document (PID) Approved	N/A
Environmental Clearance (PA/ED)	Nov 2021
Final Design Approved (RTL)	July 2023
Construction Notice to Proceed	Feb 2024
Complete for Beneficial Use	[Oct 2026]
End of Project	[Nov 2026]

Budgetary Estimate At Completion (\$ 000's)	
Cost Item	Amount
Project Report	N/A
Final Design	\$829
Construction	\$9,919
Total	\$10,748

Funding Estimate At Completion (\$ 000's)	
Funding Source	Amount
Federal ATP	\$6,132
TDA Article 3	\$385
City Contributions	\$1,525
TIRCP	\$3,171
TBD	\$(465)
Total	\$10,748

Board Approved Funding: \$11,213,000

Project Notes of Interest:

- SBCTA is leading both the design and construction phases.
- Each of the five cities are providing funding for support costs to the project.

Lead Agency SBCTA

Project Manager Juan Lizarde (909) 884-8276
jlizarde@gosbcta.com

Public/Media Contact Tim Watkins (909) 884-8276
twatkins@gosbcta.com

HIGHLAND/REDLANDS REGIONAL GAP CONNECTOR PROJECT

Map of Project:



Project Scope Summary:

Construct new active transportation improvements (ATP) including bicycle and pedestrian paths connecting the existing ATP facilities in City of Highland to City of Redlands.

Project Benefit:

Directly impact students using non-motorized transportation to access Citrus Valley High School.

Project Status and Continuing Activities:

- SBCTA expects to receive Board approval of Cooperative Agreement with the City of Highland and City of Redlands.
- City of Highlands is leading the design efforts and is in negotiations with the design firm.
- SBCTA will award the Construction Management services contract January 2026 Board meeting.
- The construction contract is expected to be awarded in Summer of 2026.

Project Notes of Interest:

- SBCTA expects to receive \$3 million in Mobile Source Air Pollution Reduction Review Committee (MSRC) funds in November 2025.
- SBCTA is seeking \$2 million in Community Project Funding (CPF) funds in 2026 Federal Appropriations.

Schedule Summary	
Milestone	Actual [Forecast]
Start of Project	Nov 2017
Project Initiation Document (PID)	Dec 2020
Environmental Clearance (PA/ED)	Dec 2022
Final Design Approved (RTL)	[Feb 2026]
Construction NTP	[Sep 2026]
Complete for Beneficial Use	[Aug 2027]
End of Project	[Apr 2028]

Budgetary Estimate At Completion (\$000's)	
Cost Item	Amount
Environmental Mitigation	\$1,500
Final Design	\$0
ROW	\$0
Construction	\$7,500
Total	\$9,000

Funding Estimate At Completion (\$000's)	
Funding Source	Amount
Measure I	\$9,000
MSRC [Funds are pending, if awarded will reduce Measure I]	[\$3,000]
CPF [Funds are pending, if awarded will reduce Measure I]	[\$2,000]
Total	\$9,000

Board Approved Funding: \$9,000,000

Lead Agency: SBCTA

Project Manager: Jeffery Hill
(909) 884-8276
jhill@gosbcta.com

Public/Media Contact: Tim Watkins (909) 884-8276
twatkins@gosbcta.com



1170 West Third Street, Second Floor
San Bernardino, California 92410-1715
Telephone: (909) 884-8276
www.gosbcta.com
